ID	Task Name	Duration	Start	Finish	Predec	Resource Names
1	**MMPC Intranet Site**	**132 days**	**Mon 17/04/03**	**Tue 17/10/03**		
2	**Initiating Process**	**8 days**	**Mon 17/04/03**	**Wed 17/04/12**		
3	Identify key stakeholders	1 day	Mon 17/04/03	Mon 17/04/03		Mo Mulundi ,Nandi Muller
4	Prepare project charter	4 days	Tue 17/04/04	Fri 17/04/07	3	Administrative Assistant,Mo
5	Hold project kick-off meeting	3 days	Mon 17/04/10	Wed 17/04/12	4	Administrative Assistant,Andile Rabada,Human
6	**Planning Process**	**93 days**	**Thu 17/04/13**	**Mon 17/08/21**	**2**	
7	Scope Statement	2 days	Thu 17/04/13	Fri 17/04/14	2	Jaqui Jacks,Mo Mulundi ,Nandi
8	Team planning meeting	1 day	Thu 17/04/13	Thu 17/04/13	2	Administrative Assistant,Andile
9	**Schedule, Cost baseline and risk**	**12 days**	**Thu 17/04/13**	**Fri 17/04/28**	**2**	
10	Determine task resources	3 days	Thu 17/04/13	Mon 17/04/17	2	Human Resources Director,IT Director,Jaqui
11	Determine task durations	2 days	Tue 17/04/18	Wed 17/04/19	10	IT Director,Nandi Muller,Kevin Desai
12	Determine dependencies	2 days	Thu 17/04/20	Fri 17/04/21	11	Administrative Assistant,Jaqui
13	Create Gantt chart	5 days	Mon 17/04/24	Fri 17/04/28	12	Jaqui Jacks,Nandi Muller
14	**Risk Assesment**	**10 days**	**Mon 17/05/01**	**Fri 17/05/12**	**13**	
15	Identify risks	5 days	Mon 17/05/01	Fri 17/05/05	13	Administrative Assistant,Andile
16	Discuss risks	3 days	Mon 17/05/08	Wed 17/05/10	15	IT Director,Jaqui Jacks,Michael
17	Prioritise risks	2 days	Thu 17/05/11	Fri 17/05/12	16	IT Director,Michael Chen,Mo Mulundi
18	**Gathering User info**	**83 days**	**Thu 17/04/13**	**Mon 17/08/07**	**5**	
19	Gather user requirements	38 days	Thu 17/04/13	Mon 17/06/05	5	Administrative Assistant,Nandi
20	Develop survey	25 days	Tue 17/06/06	Mon 17/07/10	19	Jaqui Jacks,Michael Chen,Nandi Muller
21	Execute survey	10 days	Tue 17/07/11	Mon 17/07/24	20	Administrative Assistant,Nandi
22	Survey analysis	10 days	Tue 17/07/25	Mon 17/08/07	21	IT Director,Jaqui Jacks,Nandi
23	Test Developement	10 days	Tue 17/08/08	Mon 17/08/21	18	IT Director,Kevin Desai,Michael
24	**Executing Process**	**79 days**	**Tue 17/08/08**	**Fri 17/11/24**	**18**	
25	**Intranet Site**	**79 days**	**Tue 17/08/08**	**Fri 17/11/24**	**18**	
26	**Intranet Site Development**	**50 days**	**Tue 17/08/08**	**Mon 17/10/16**	**18**	
27	**Templates & Tools**	**50 days**	**Tue 17/08/08**	**Mon 17/10/16**	**18**	
28	Examples	20 days	Tue 17/08/08	Mon 17/09/04	18	Kevin Desai
29	Files	20 days	Tue 17/09/05	Mon 17/10/02	28	Sindi Ndlovu
30	Instructio	10 days	Tue 17/10/03	Mon 17/10/16	29	Kevin Desai,Sindi Ndl
31	**Ask the Expert feature**	**50 days**	**Tue 17/08/08**	**Mon 17/10/16**	**18**	
32	Expert database creation	20 days	Tue 17/08/08	Mon 17/09/04	18	Human Resources Director,Michael Chen,Nandi Muller

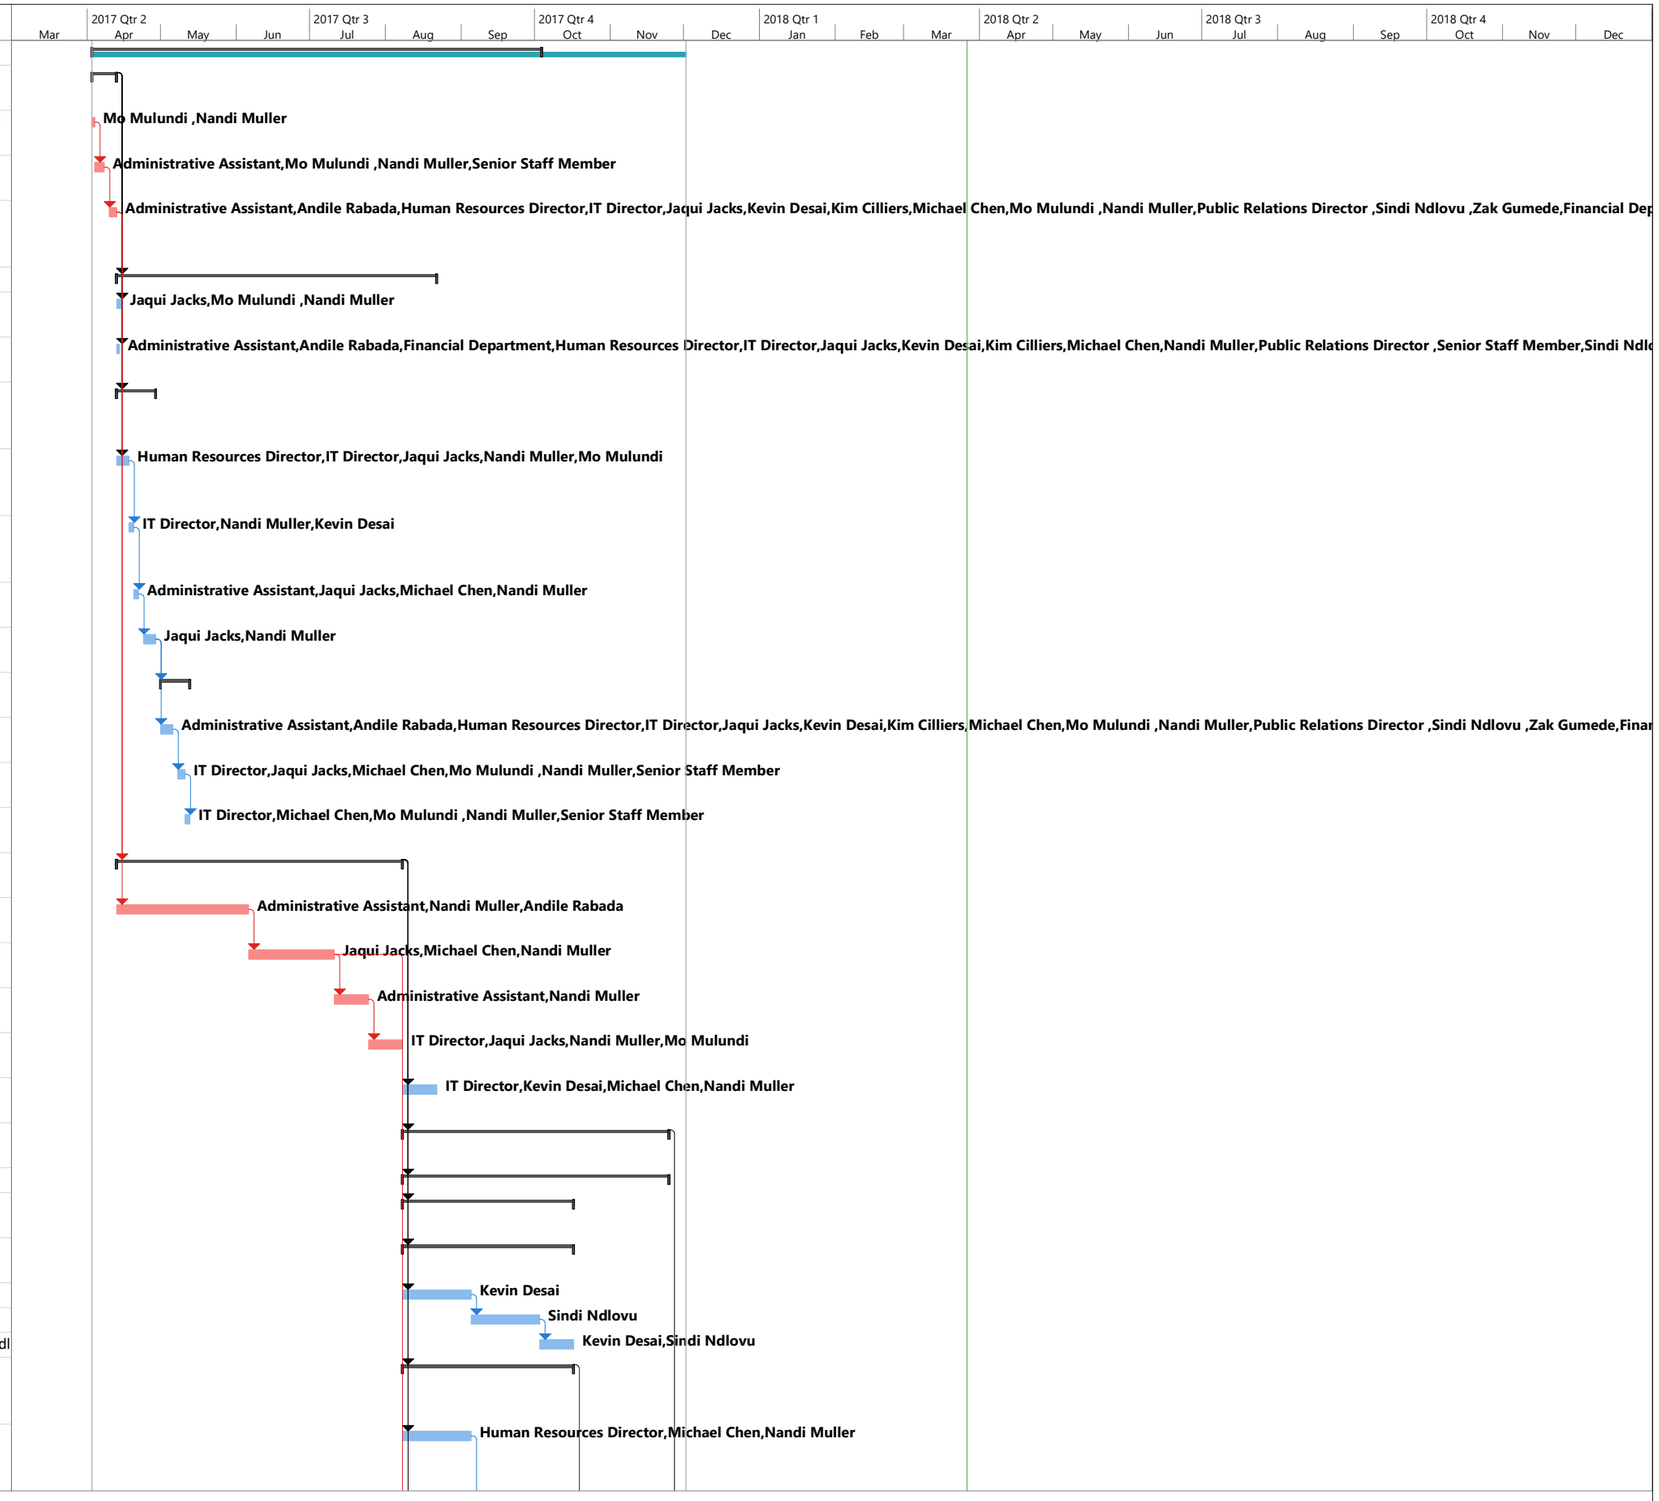

Project: MECNProject
Date: Tue 18/03/27

Task		Summary		Inactive Milestone		Duration-only		Start-only		External Milestone		Critical Split	
Split		Project Summary		Inactive Summary		Manual Summary Rollup		Finish-only		Deadline		Progress	
Milestone		Inactive Task		Manual Task		Manual Summary		External Tasks		Critical		Manual Progress	

ID	Task Mode	Task Name	Duration	Start	Finish	Predec	Resource Names
33		Payment method for ask the expert feature	20 days	Tue 17/09/05	Mon 17/10/02	32	Michael Chen,Financial Department
34		Expert database connectio	10 days	Tue 17/10/03	Mon 17/10/16	33	Andile Rabada
35		Ask The Expert Feature Complete	0 days	Mon 17/10/16	Mon 17/10/16	31	
36		User Request feature	50 days	Tue 17/08/08	Mon 17/10/16	18	Andile Rabada,Nandi Muller
37		Search feature	15 days	Tue 17/08/08	Mon 17/08/28	18	Kevin Desai
38		User submission feature	20 days	Tue 17/08/08	Mon 17/09/04	18	Sindi Ndlovu
39		**Security**	**15 days**	**Tue 17/08/08**	**Mon 17/08/28**	**18**	
40		Payment method to allow full site access	15 days	Tue 17/08/08	Mon 17/08/28	18	Financial Department,Sindi Ndlovu
41		Site access control	7 days	Tue 17/08/08	Wed 17/08/16	18	Andile Rabada,Sindi Ndlovu
42		**Intranet Site Design**	**17 days**	**Tue 17/08/08**	**Wed 17/08/30**	**18**	
43		Site Map	8 days	Tue 17/08/08	Thu 17/08/17	18	Andile Rabada,Kevin
44		Suggested Formats	6 days	Fri 17/08/18	Fri 17/08/25	43	Kim Cilliers,Sindi Ndlovu
45		Graphics	3 days	Mon 17/08/28	Wed 17/08/30	44	Jaqui Jacks,Kevin Desai
46		Intranet Site Construction	48 days	Thu 17/08/31	Mon 17/11/06	42	Kevin Desai,Michael Chen,IT Director
47		Intranet Site Testing	14 days	Tue 17/11/07	Fri 17/11/24	46	Andile Rabada,Nandi Muller,Sindi Ndlovu
48		Testing Complete	0 days	Fri 17/11/24	Fri 17/11/24	47	
49		**Articles**	**45 days**	**Tue 17/08/08**	**Mon 17/10/09**	**18**	
50		Development of article content	40 days	Tue 17/08/08	Mon 17/10/02	18	Jaqui Jacks,Sindi Ndlovu
51		Sourcing of links	5 days	Tue 17/10/03	Mon 17/10/09	50	Administrative Assistant,Nandi Muller
52		**Monitoring & Controlling Process**	**82 days**	**Tue 17/08/08**	**Wed 17/11/29**	**18**	
53		Milestone Report	1 day	Tue 17/08/08	Tue 17/08/08	20	Mo Mulundi ,Nandi Muller
54		Final Report	3 days	Mon 17/11/27	Wed 17/11/29	24	Mo Mulundi ,Nandi M
55		Project benefits measurements	30 days	Tue 17/08/08	Mon 17/09/18	18	Nandi Muller
56		**Closing Process**	**5 days**	**Mon 17/11/27**	**Fri 17/12/01**	**47**	
57		**Release**	**5 days**	**Mon 17/11/27**	**Fri 17/12/01**	**47**	
58		Promotion	5 days	Mon 17/11/27	Fri 17/12/01	47	Administrative Assist
59		Roll Out	5 days	Mon 17/11/27	Fri 17/12/01	47	Administrative Assist

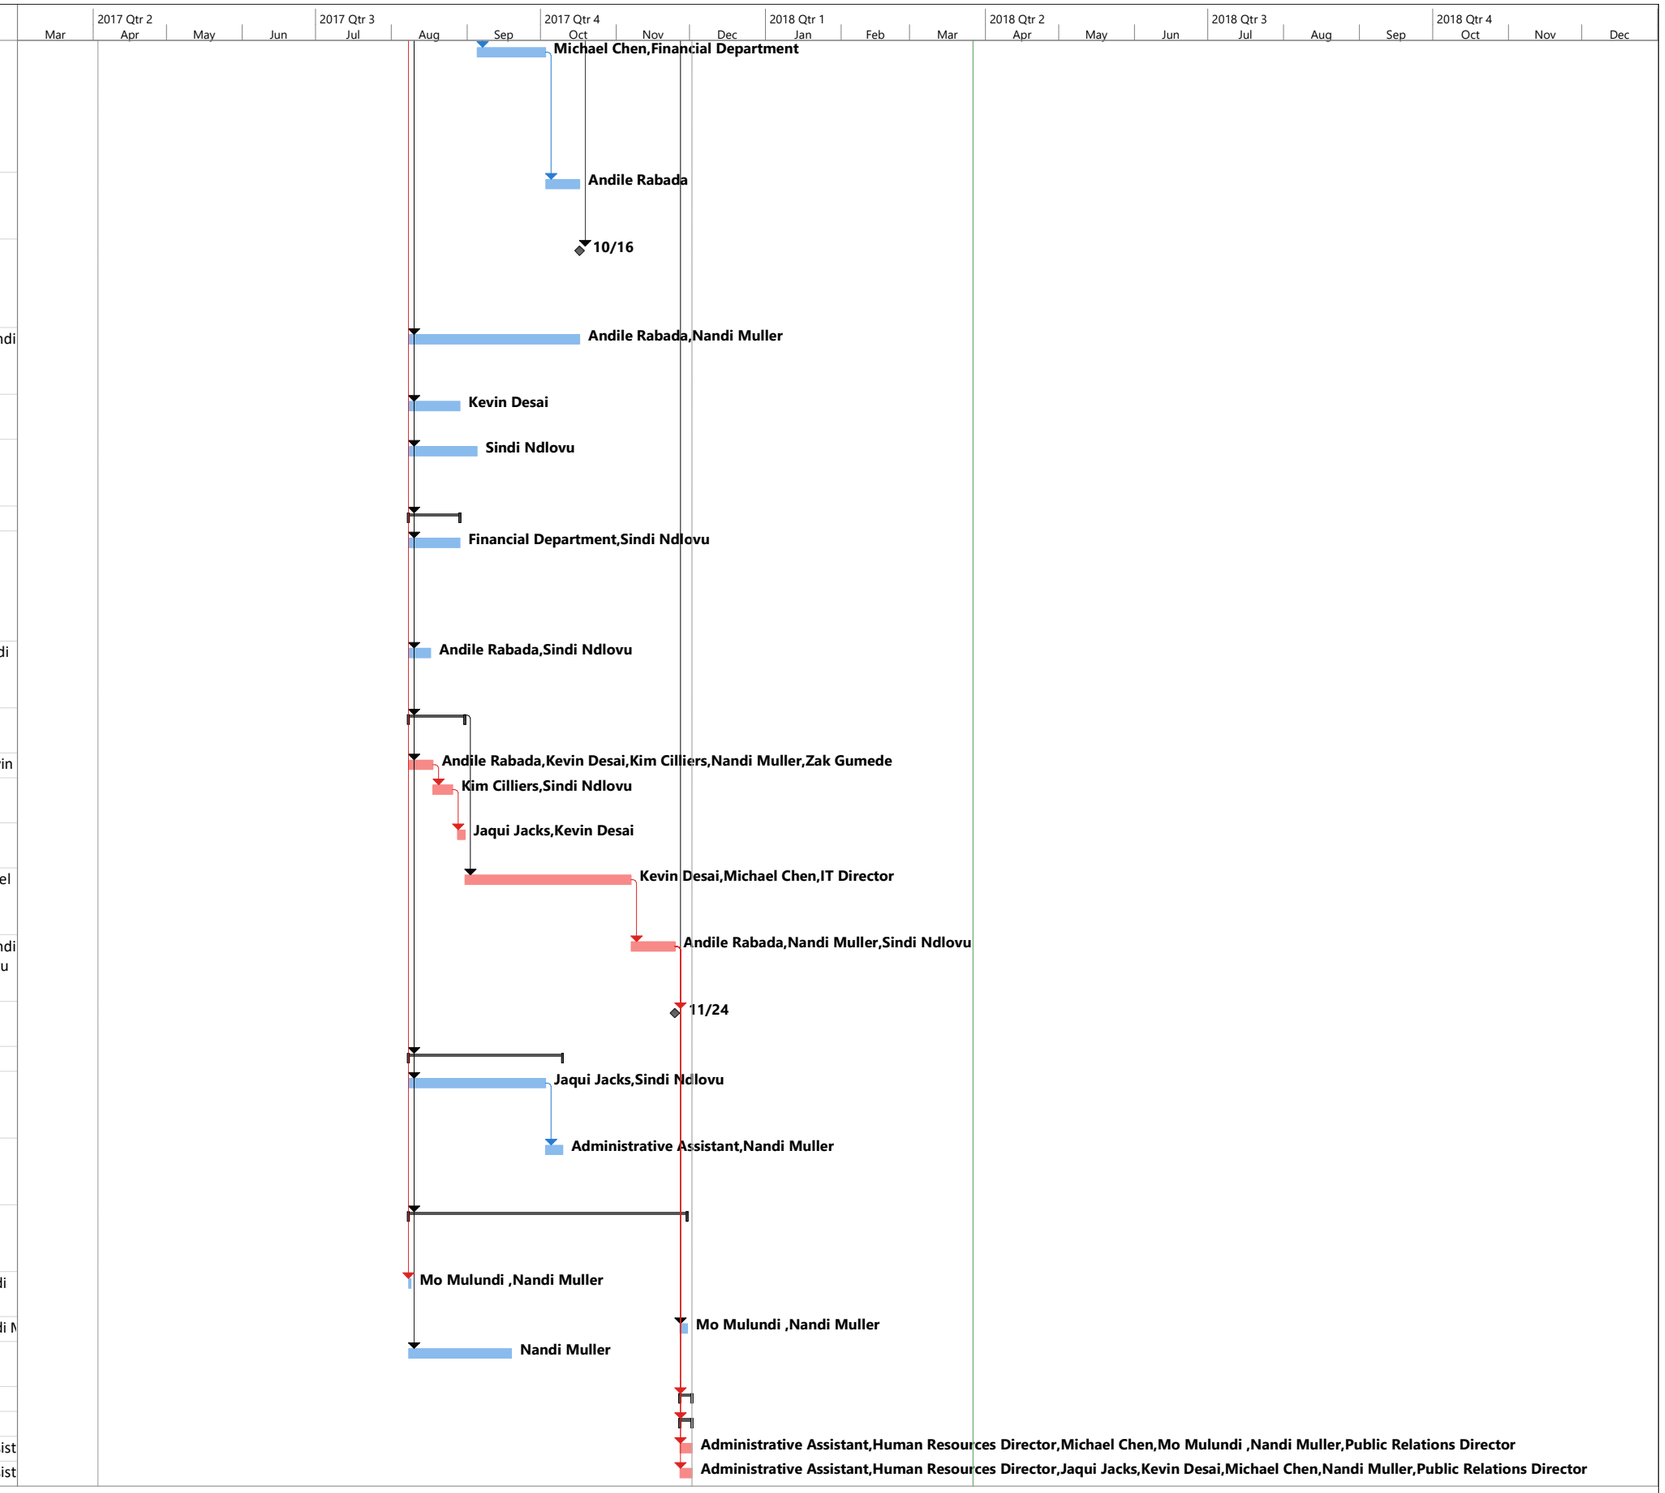

Project: MECNProject
Date: Tue 18/03/27

Task		Summary		Inactive Milestone		Duration-only		Start-only		External Milestone		Critical Split	
Split		Project Summary		Inactive Summary		Manual Summary Rollup		Finish-only		Deadline		Progress	
Milestone		Inactive Task		Manual Task		Manual Summary		External Tasks		Critical		Manual Progress	
